

A BUDGET OF FRIVOLITIES



Citizens Report on Budgets and Projects of
the Niger Delta Development Commission

2020

A BUDGET OF FRIVOLITIES

**Citizens Report on Budgets and Projects of
the Niger Delta Development Commission**



Copyright © 2023 Social Development Integrated Centre (Social Action)

All rights reserved

ISBN: 978-978-791-476-2

Published by:

Social Development Integrated Centre (Social Action)

33, Oromineke Layout, D-Line

Port Harcourt, Nigeria

Tel/Fax +234 84 765 413

www.saction.org

Design and layout: Dezipn Hall

CONTENTS

ACKNOWLEDGEMENT	iii
BACKGROUND	1
2020 Economic Outlook and the COVID-19 Pandemic	1
THE NDDC	3
The 2020 NDDC Budget	3
Analysis of the 2020 NDDC Budget	3
Sources of Revenue for NDDC 2020 Budget	4
Development Projects Capital Analysis	4
Summary of NDDC Project Allocations to States and the Regional Head Quarters	5
REGIONAL	6
Vague/Frivolous Budget Allocations	6
BAYELSA STATE CAPITAL ALLOCATION	7
BAYELSA STATE Development Projects	7
EDO STATE CAPITAL ALLOCATION	9
EDO STATE Development Projects	9
CROSS RIVERS STATE CAPITAL ALLOCATION	11
CROSS RIVERS STATE Development Projects	11
IMO STATE CAPITAL ALLOCATION	13
IMO STATE Development Projects	13
BUDGET MONITORING REPORT	14
Bayelsa State	14
Edo State	17
Imo State	19
Ondo State	21
NDDC TRACKED PROJECT IMAGE GALLERY	23
Bayelasa State Project Images	23
Edo State Project Images	26
Imo State Project Images	29
Ondo State Project Images	31

ACKNOWLEDGEMENT

This volume contains summaries of analysis and monitoring reports of projects included in the 2020 annual budget of the Niger Delta Development Commission (NDDC), as conducted by members, community volunteers and associates of the Social Development Integrated Centre (Social Action) and its Anti-Corruption Network partners in the Niger Delta region. Organisations that supported the monitoring process included Niger Delta Budget and Citizens Platform, Action for Socio-Political and Economic Change (ASEC) Edo State; Delta Civil Anti-Corruption Network; Global Care Rescue Mission, Bayelsa; Imo NDDC Advocates; Ondo Budget Transparency and Accountability Platform (OBTAP); Better Common Life Initiative (BECOLIN) and Bayelsa NDDC Projects Monitoring Platform.

This report is written by Botti Isaac.

The analysis of the 2020 budget of the NDDC was conducted by Botti Isaac, Peter Mazzi, Precious Charles and Comfort Agbebaku

Members of the teams of project monitors in the states of the Niger Delta included Osazee Edigin, Umoren Uduak, Lucky Igbecha, Aliyu Umweni, Omobude Agho, Boney Akaeze, Chibundu Uchegbu, Uchenna Njoku, Basil Ejigini, , Eloho Yvonne Ibiyinka, Stella Ikeokwu Nathaniel, Akintomide Jerry, Comr Princess Elizabeth Egbe, Authority Benson, Abigail Oputa, Iyala Ikisikpo, Anita D., Ftyin Otokito, Ogosi Roseline, Faith Effiong and Duke Fakegha

Social Action's management staff, Anino Mercy Atsekurubu and Peter Mazzi supported the report development process.

This report is produced in the frame of the Promoting Transparency and Accountability through Collective Action in Communities in Nigeria, which is supported by the MacArthur Foundation.

The views contained in this publication are those of Social Action.





BACKGROUND

2020 Economic Outlook and the COVID-19 Pandemic

The global growth of 2.9 percent in 2019 was reversed, owing to the devastating effect of the COVID-19 pandemic. Against the backdrop of the COVID-19 outbreak, the global economy contracted by 3.1 percent in 2020, largely driven by advanced economies, which recorded a contraction of 4.4 percent in the year. This had a significant toll on the global economy as trade and investment activities leading economic stagnation. Just like many other countries, Nigeria was not spared the impact of COVID-19. In 2020, the economy halted its 12 consecutive quarters of expansion and contracted by 6.1 percent in 2020 Q2, mainly driven by the plunge in global oil prices and the prolonged enforcement of lockdowns and stringent restrictions the world over. In 2020 Q3, the Nigerian economy fell into a recession with a second consecutive negative growth of -3.6 percent (-6.1 percent in 2020 Q2). This represents the second economic contraction since 2016. Cumulatively, the economy contracted by 1.9 percent in the full year of 2020, compared to an expansion of 2.3 percent in 2019.^[1] Like every economy of the world, the Nigerian economy faced significant challenges in 2020 arising from the COVID-19 pandemic and its global impact.

The pandemic exacerbated key negative economic realities such as inflation, unemployment, a tightening fiscal space, and a wavering currency value in the face of dwindling public revenue. With the significant macroeconomic challenges that faced the nation, critical steps were taken to promote economic recovery, sustained growth, and socio-economic development. This includes revising the year's budget to accommodate the exigencies from Covid-19, as well as embarking on priority programmes in areas that are important in attracting private investment to sustain growth and development in the short and long term. These priority areas are macroeconomic stability, policy and regulatory consistency, sector reforms, and human capital development. Sectoral reforms and investment in human capital development were promoted to support improved economic outcomes in the medium to long run and for maximizing the productive capacity of the nation.

The effects of the COVID-19 pandemic on economic activities, significantly worsened Federation revenue, particularly nonoil receipts in the first half of 2020. Non-oil revenue, at N1.868 billion (2.7 percent of GDP), declined by 43.5 percent below its benchmark, owing to shortfalls in Corporate Tax, Value-Added Tax, and Customs and Excise Duties. The total debt outstanding by the Federal Government stood at N24.522 billion in end-March 2020,

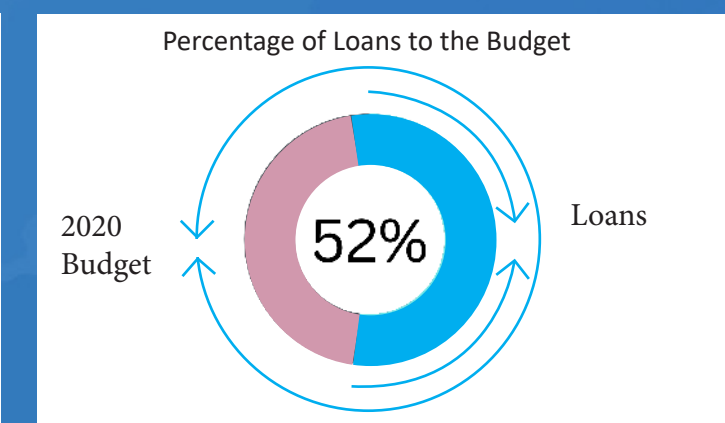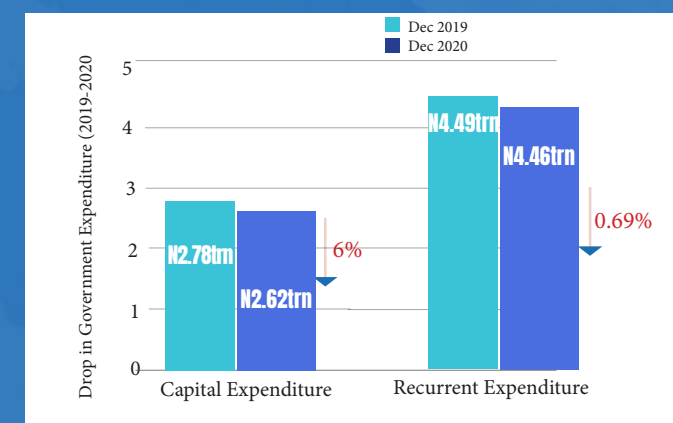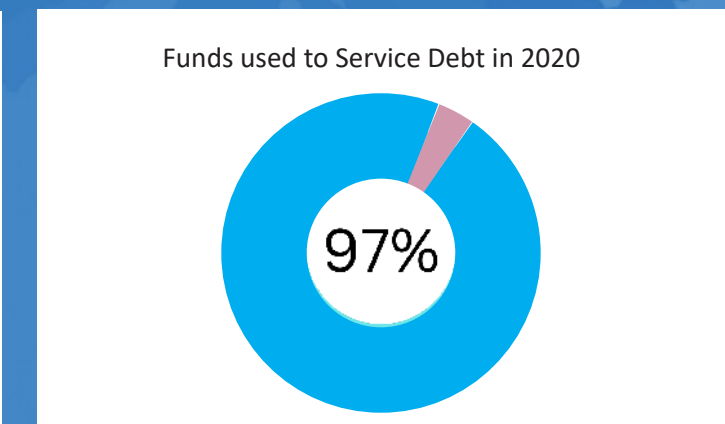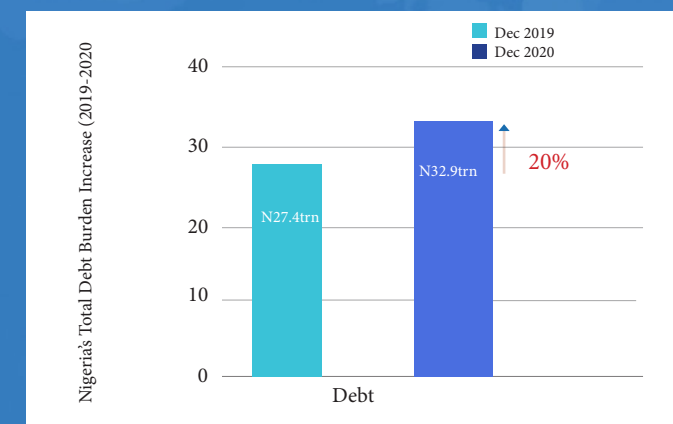

Petroleum Corporation from crude oil and gas exports in 2020 plunged by 45.98 percent due to the COVID-19-induced collapse in price and demand. This, therefore, impacted significantly on revenue generation from the sector. Nigeria's revenue from the exports of crude oil and gas fell to \$2.62bn in 2020 from \$4.85bn in 2019.²

The rising fiscal deficit occasioned by the economic impact of the Covid-19 pandemic heightens the spate of public borrowings in Nigeria and resulted in a significant increase in public debt figures during the period. Nigeria's total debt burden as of December 2019 was N27.4 trillion³, however, due to dwindling oil revenue, Nigeria's Government resorted to borrowings to augment its budget. As of the end of 2020, Nigeria's total public debt rose by 20% to

N32.9 billion⁴. This figure represented 50% of the 2020 National Budget. In other words, N5.5 trillion was borrowed to partly finance the N10.5 trillion budgets in 2020. Despite the shortfall in government revenue, it is significant to also state that the federal government used 97% of its revenue to service public debt in 2020.⁵ This had a severe toll on government capital expenditure, hence the increased borrowing. The impact of the Covid-19 pandemic was felt in the drop in government expenditure, for instance, the year's capital expenditure was reduced by N155 billion from N2.78 trillion to N2.62 trillion while recurrent expenditure was reduced by N25 billion from N4.49 billion to N4.46 billion.⁶

1 <https://www.cbn.gov.ng/Out/2020/RSD/CBN%20Economic%20Report%20Half%20Year%202020.pdf>

2 <https://punchng.com/oil-gas-export-revenue-fell-by-2-23bn-in-2020-nnpc/#:~:text=Nigeria's%20revenue%20from%20the%20exports,and%20demand%20for%20the%20commodity.>

3 <https://dmo.gov.ng/debt-profile/total-public-debt/3123-nigeria-s-total-public-debt-stock-as-at-december-31-2019/file>

4 <https://dmo.gov.ng/debt-profile/total-public-debt/3491-nigeria-s-total-public-debt-stock-as-at-december-31-2020/file>

5 <https://www.premiumtimesng.com/news/top-news/472929-nigeria-spent-97-of-revenue-on-debt-servicing-in-2020-report.html?tztc=1>

6 <https://www.premiumtimesng.com/news/headlines/386844-nigeria-reduces-2020-budget-slashes-revenue-projection-by-40.html?tztc=1>

THE NDDC

The Niger Delta region is home to over 20 million people, most of who are engaged in subsistence farming and fishing. However, the region is also rich in oil and gas reserves, which are the primary source of revenue for the Nigerian government. Despite the wealth generated by these resources, the region has seen little development, while poverty and unemployment rates remain high. Additionally, decades of oil spills and gas flaring have had a devastating effect on the environment, with many communities facing health and economic challenges as a result. The region is known for its vast oil and gas resources, but also its poverty, environmental degradation, and lack of infrastructure and basic services.

The NDDC was created to promote sustainable development in the Niger Delta region. It is responsible for planning, coordinating, and implementing development projects in the areas of infrastructure, human capital development, and environmental protection. The commission's primary focus is on addressing poverty, unemployment, and environmental degradation. To achieve this, the NDDC implements a variety of programs and projects, including infrastructure development, education and training, and community development.

However, years of budget formulation, appropriation, and implementation have not brought the desired change to the Niger Delta. Hint from the Forensic Audit Report revealed that 87% of the projects implemented by NDDC between 2001 and 2019 were abandoned.⁷ A major factor responsible for this is corruption coupled with a weak management structure. This is no wonder why the yearly revenue accruing to NDDC has not had any significant impact on the region. In 2019, the NDDC received a total capital budgetary allocation of N306.5 billion to implement some 5,956 projects across the nine states including its regional capital projects. 90% of these projects were carried over from the previous year which implies that many of the projects were started many years ago and budgetary allocations are being made to them every year. This calls to question the NDDC budget formulation template. This does not reflect in a real sense of the zero base approach and has continued to fuel corruption and mismanagement in the NDDC system. A budget monitoring exercise conducted by Social Action revealed that 47% of the projects tracked did not


exist, 22% were abandoned, 4% were ongoing and just 26% were completed.⁸ This shows clearly the level of rot in the NDDC project implementation process. This appears to be the trend around NDDC projects and operating contrary to its motto "... *determined to make a difference...*"

The 2020 NDDC Budget


The NDDC 2020 Budget was presented in November 2019 alongside the 2019 budget. However, due to several issues bordering on perceived sharp practices by the management of the commission, the passage of the 2020 budget was delayed for a whole year. The lawmakers cited administrative illegalities and the failure of the Commission to present its 2019 Budget Performance report as major reasons for the delay in the passage of the budget. However, despite the details of the 2019 budget performance remaining sketchy, the 2020 NDDC budget was passed on December 21, 2020, ten days before the end of the year and three months before the expiration of the budget year.

Analysis of the 2020 NDDC Budget

The 2020 NDDC budget had a total approved budget outlay of N453.2 billion. A breakdown of the budget shows that N27.389 billion for Personnel expenditure and Overhead expenditure of N13.937 billion making a total N40.1 billion recurrent expenditure. This represents 9% of the total budgetary allocations. Allocation to Internal Capital expenditure of N2.793 billion was approved for the 2020 budget year while N409.08 billion was earmarked for Development projects. In other words, development projects gulped 90% of the total budget outlay for 2020.

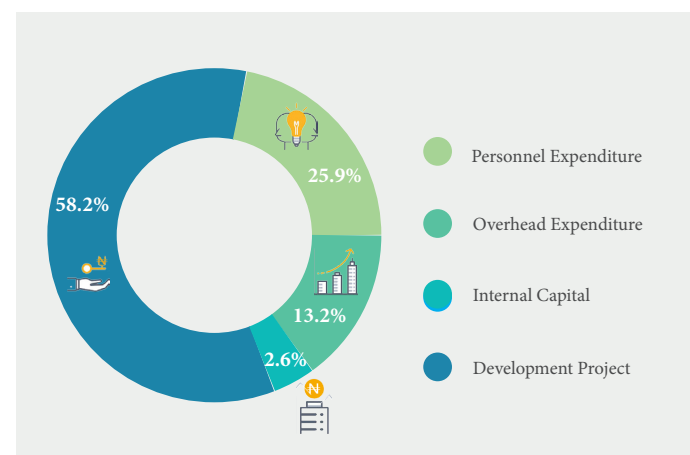

Sources of Revenue for NDDC 2020 Budget

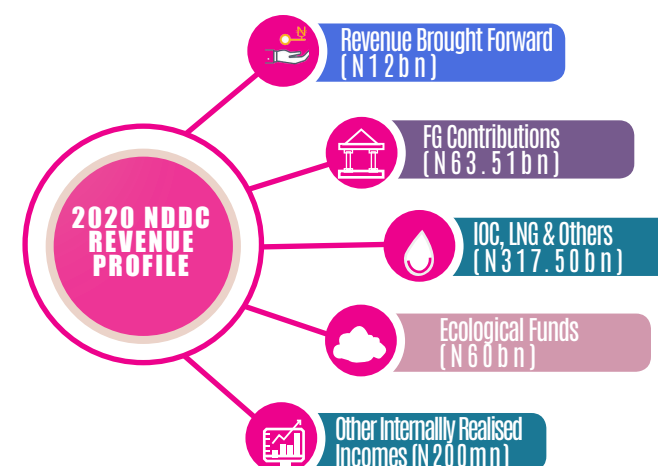


The 2020 NDDC Revenue Profile shows Revenue Brought Forward of N12 billion. Federal Government contribution of N63.506billion; Oil Companies contributions and Nigeria Liquefied Natural Gas Ltd (NLNG) and others N317.493billion; Ecological Funds of N60billion; and Other Internally Realized Income of 200million.

Further analysis of the Internal Capital Expenditure shows that allocations to motor vehicles alone gulped N1.7 billion, representing about 61% of the total internal capital allocation. Equipment allocation is N356.156 million, representing 13% of the internal capital allocation. The remaining N726.821 billion, representing 26% was allocated to furniture, "others", building construction, and Generator. While a the sum of N1.7 billion was allocated to the purchase of 49 new vehicles, NDDC under its recurrent expenditure allocated a whopping sum of N2.361 billion to motor vehicle maintenance (under the Chairman's office). Another disturbing trend in the budget is the allocation of N1.208 billion to Newspapers and Periodicals as part of its recurrent expenditure (Chairman's office). It also allocated the sum of N1.2 billion for repairs and maintenance of Residential Quarters (Chairman's Office) even when only N249 million was allocated to building construction (including 3 state office buildings), and head office extension in the internal capital allocation.

Development Projects Capital Analysis

The 2020 Development Projects has a total capital allocation of N409.08billion, representing the entire 90% of the total approved budgetary allocation to NDDC. The 2020 capital allocation represents a 34%

increase from the previous year. A further look shows that Delta state got a total of N61.5 billion, followed by Akwa Ibom with N49.1 billion. Bayelsa got a total of N42.3 billion while Rivers State got a total of N41.3 billion. Edo state got a total of N20.1 billion while Ondo state got a total of N18.05 billion. States with the lowest allocations include Abia with N16.1 billion, Imo with N15.2 billion while Cross River got the least allocation of N12.7 billion. However, 32% of the capital allocation was approved for Head Office/Regional projects with a total budget figure of N132.3 billion.

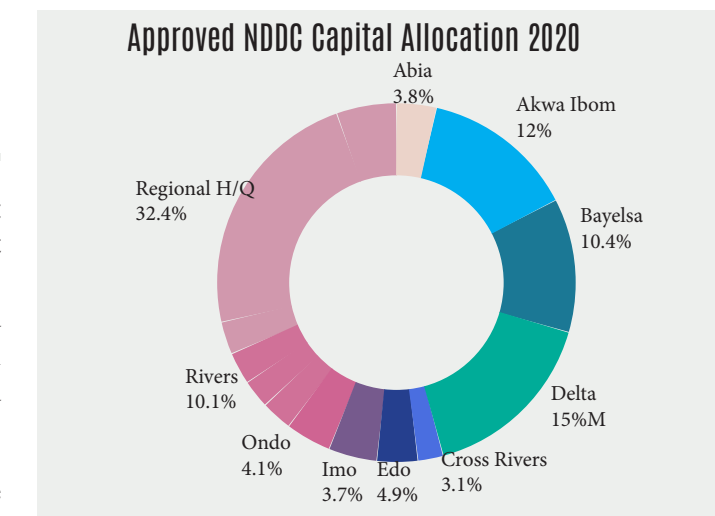


A further breakdown of the Regional budget allocations shows that some 459 projects were to be executed in states and communities across the Niger Delta. These projects cut across sectors such as Agric/Fisheries, Canalization/Reclamation, Community and Rural Development, Ecology, Education, Energy, and Power. Others are ICT, Industrial and Enterprise Development, Roads and Bridges, etc. A cursory look at the allocations to each subsector showed where the priority of NDDC lay during that budget year. Roads and Bridges construction took 40% of the regional budget allocations with a total figure of N52.8 billion. This was followed by Industries and Enterprises with N11.5 billion. The Health sub-sector has a total N10.5 billion representing 7% of the regional allocation. This is particularly interesting because the year 2020 saw the outbreak of the COVID-19 pandemic and the health challenges it threw up. So it is expected that NDDC will allocate not less than 20% of its budget to financing health gaps or curtailing the spread of covid-19 during the period. This shows how misplaced NDDC priority is in 2020, particularly since it could have taken advantage of the late passed request adjustment in health budget allocation. The sector of education suffered a similar fate with just N6.6billion capital allocation

⁷ <https://businessday.ng/news/article/why-12000-nddc-projects-were-abandoned/>

⁸ <https://saction.org/books/Pond-of-Crocodiles5.pdf>

Summary of NDDC Project Allocations to States and the Regional Head Quarters

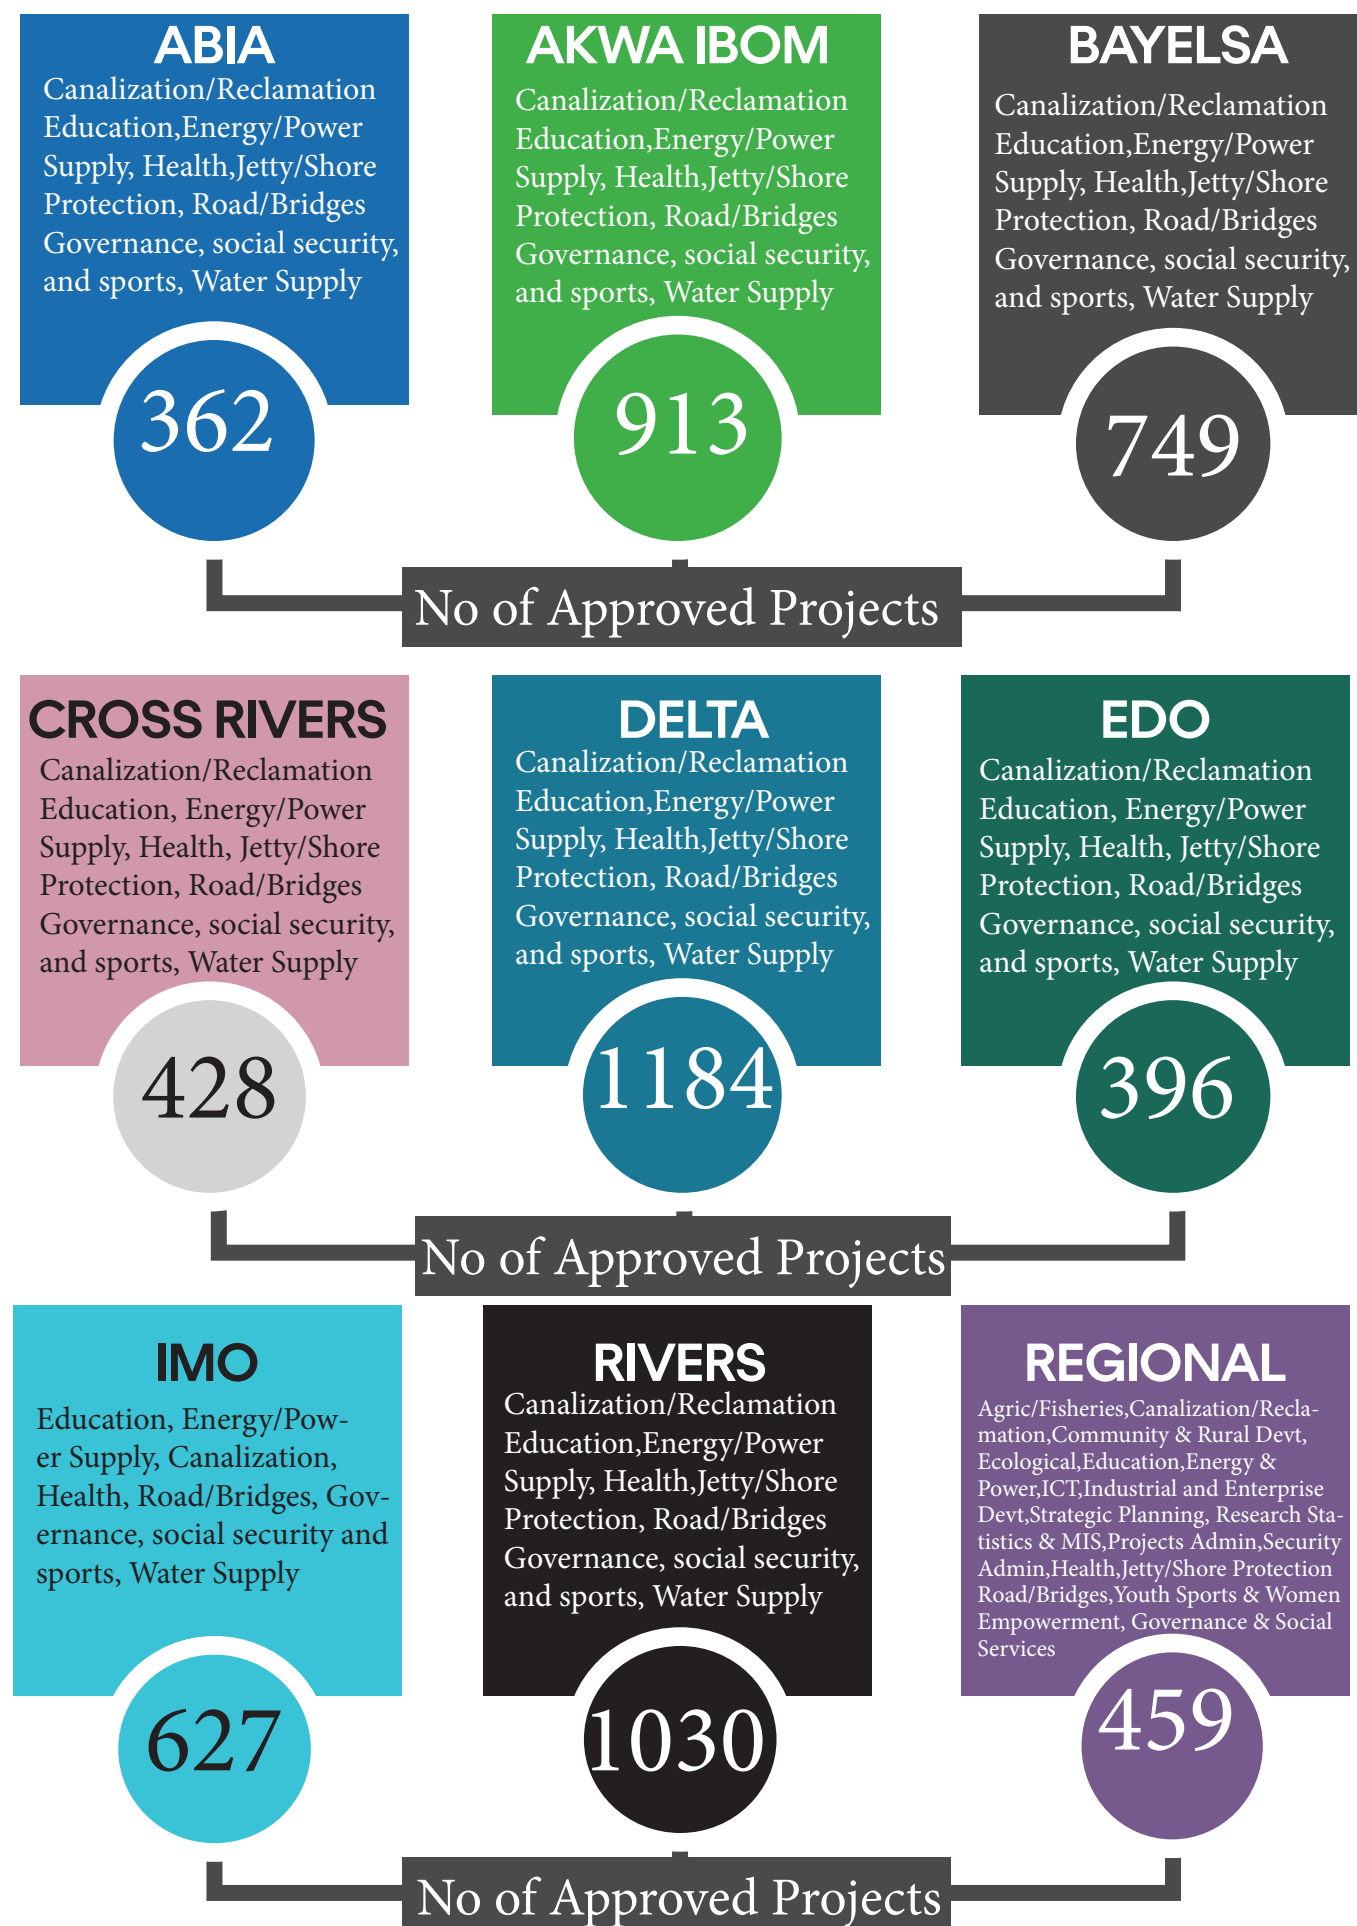

REGIONAL

S/NO	PROJECT TYPE	NUMBER OF PROJECTS	TOTAL AMOUNT
1	Agric/Fisheries	15	7,197,633,69-
2	Canalization/Reclamation	28	4,541,160,000
3	Community & Rural Development	6	262,950,000
4	Ecological	10	682,500,000
5	Education	18	6,671,264,725
6	Energy and Power Supply	42	10,127,795,787
7	ICT	21	1,294,415,000
8	Industrial and Enterprise Development	18	11,557,000,000
9	Strategic Planning, Research Statistics & Mgt. Infor. System	18	3,990,000,000
10	Projects Admin/Others	17	4,815,096,670
11	Security Admin	12	4,230,000,000
12	Health	45	10,589,180,252
13	Jetty/Shore Protection	30	4,691,245,550
14	Road/Bridges	118	52,842,947,890
15	Youth Sports and Women Empowerment	18	1,226,500,000
16	Governance & Social Services	43	7,685,310-
Grand Total		459	132,360,000,000

Vague/Frivolous Allocations

Budget


Major concerns around the Regional Project include the vagueness of project description, the lack of specificity of project locations, and the repetition of projects under different names. A deeper look at the various projects proposed under the regional projects revealed that many of the projects are vague and cannot be tracked. For instance, we see things like “Provision of small palm oil mill and processing

to viable smallholders farmer cooperatives and group”; “Establishment of NDDC Demonstration/ Integrated Farms in 9 States of the region”; “Supply of Science Equipment” etc with no details at to which states or communities these were this implemented or how many beneficiaries were covered. You also see things like “provision of solar powered street lights in selected communities in the Niger Delta – N100 million and no other details. This budget style is a recipe for corruption as it does not allow for monitoring and accountability.

BAYELSA STATE CAPITAL ALLOCATION

Bayelsa state is among the states with the highest capital allocation from NDDC. It had a total budget allocation of N42.3 billion, representing 10% of the total development projects 'allocation. It also represents a 26% increase from the 2019 allocation. The capital allocation was expected to cover 749 projects that cut across eight subsectors. A review of budget priority shows that Road and Bridges subsector received the highest allocation with the sum of N19.1 billion which represents 45% of the total budget allocation to the state. Canalization/Reclamation and Energy/Power received the next highest allocation of N5.3 billion and N4.8 billion respectively. The health sector despite the exigency of the Covid -19 situation in 2020, received one of the least attention with N3.3 billion, representing 7% of the total capital allocation to the state. The Education subsector got the least allocation of N872.03 million which is a paltry 2% of the total budget allocation.

S/NO	PROJECT TYPE	NUMBER OF PROJECTS	TOTAL AMOUNT
1	Canalization/Reclamation	18	5,350,036,334
2	Education	23	872,038,
3	Energy/Power Supply	122	4,829,040,255
4	Health	28	3,306,972,530
5	Jetty/Shore Protection	36	4,672,680,837
6	Road/Bridges	413	19,180,662,218
7	Governance, social security, and sports	42	2,940,658,524
8	Water Supply	67	1,207,307,259
Grand Total		749	42,359,396,342

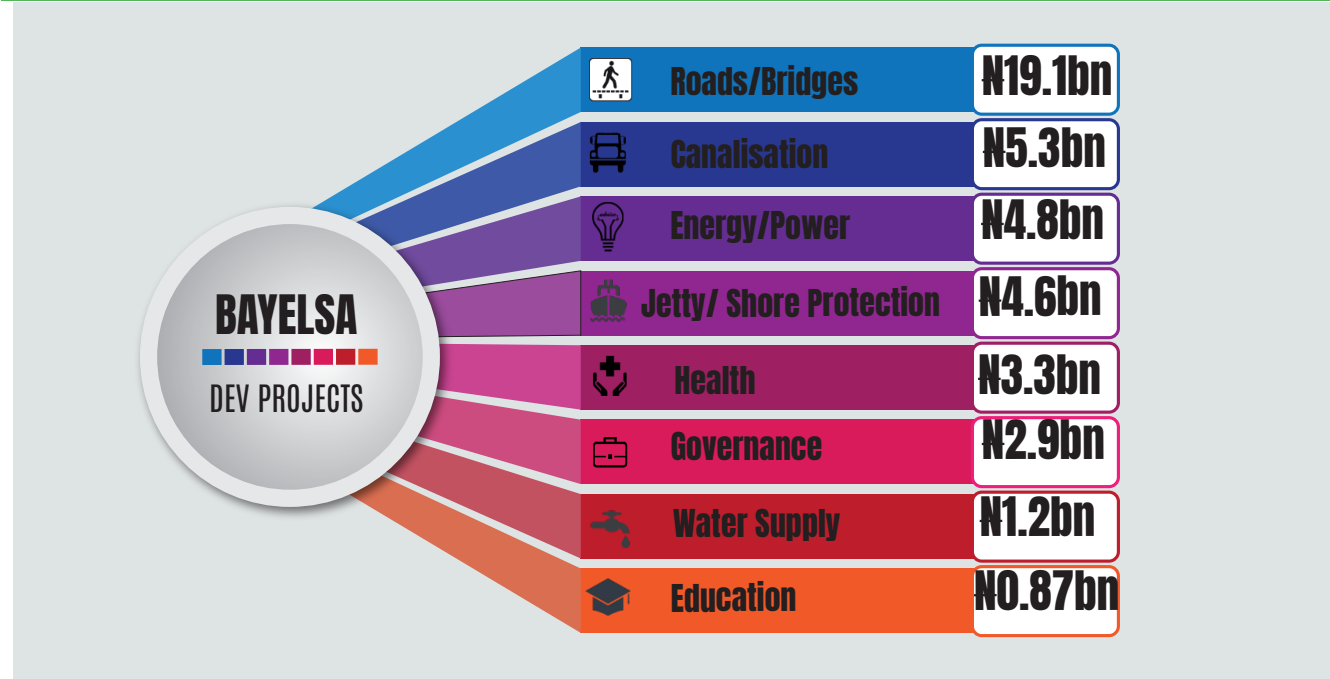

Vague and Frivolous Projects in Bayelsa


Contingency provision for de-silting of waterways and drainage systems (Lot 1-10)	Rehabilitation of dilapidated school buildings in Bayelsa state
N1.47bn	N300m
Provision of medical equipment for various cottages/health centers in Bayelsa state (Lots 1-4)	Awareness campaign workshop on unwanted teenage pregnancy, prostitution, and baby factory business in Bayelsa state. (Lot 1-8
N300m	N300m
Clearing of waterways in Bayelsa state	Contingency provision for road repairs in Bayelsa state
N150m	N446.2m
Support to celebration of World Health Days: World Health Day Celebration, World Autism Day, and World Hepatitis Day in Bayelsa state. (Lot 1-16)	Senatorial district sand search (Fixed fee contract)
N600m	N45m
Secondary school scholarship	Payment of certified IPC
N30m	N1.28bn
Skill development for rural women	Micro credit scheme for SMES
N30m	N30m
Girl child education programme	Medical outreach for all the LGA in Bayelsa state
N30m	N30m

EDO STATE CAPITAL ALLOCATION

Edo state in 2020 had a total capital budget allocation of N20.1 billion which represents 5% of the total development projects budget and 41% higher than the 2019 allocation. This budgetary allocation cuts across some 396 projects in eight subsectors. A look at the budget trend shows that Road/Bridges subsector had a total of 190 projects with N11 billion allocation. This makes the sector the highest receiver of allocation in the state. It also shows where NDDC's priority lies. The health sector in a period of crisis, as applicable to Bayelsa State, received only 8% of the total allocation with a paltry N1.8 billion. The education subsector received the least allocation of N797.7 billion after Canalization. This again shows that the NDDC 2020 budget did not take into consideration the health emergencies that Covid-19 threw up.

EDO STATE Development Projects

S/NO	PROJECT TYPE	NUMBER OF PROJ-ECTS	TOTAL AMOUNT
1	Canalization/Reclamation	4	418,434,098
2	Education	24	797,722,824
3	Energy/Power Supply	71	3,291,794,322
4	Health	23	1,882,000,000
5	Jetty/Shore Protection	1	-
6	Road/Bridges	190	11,015,751,934
7	Governance, social security, and sports	35	1,873,965,269
8	Water Supply	48	897,075,000
Grand Total		396	20,176,743,447

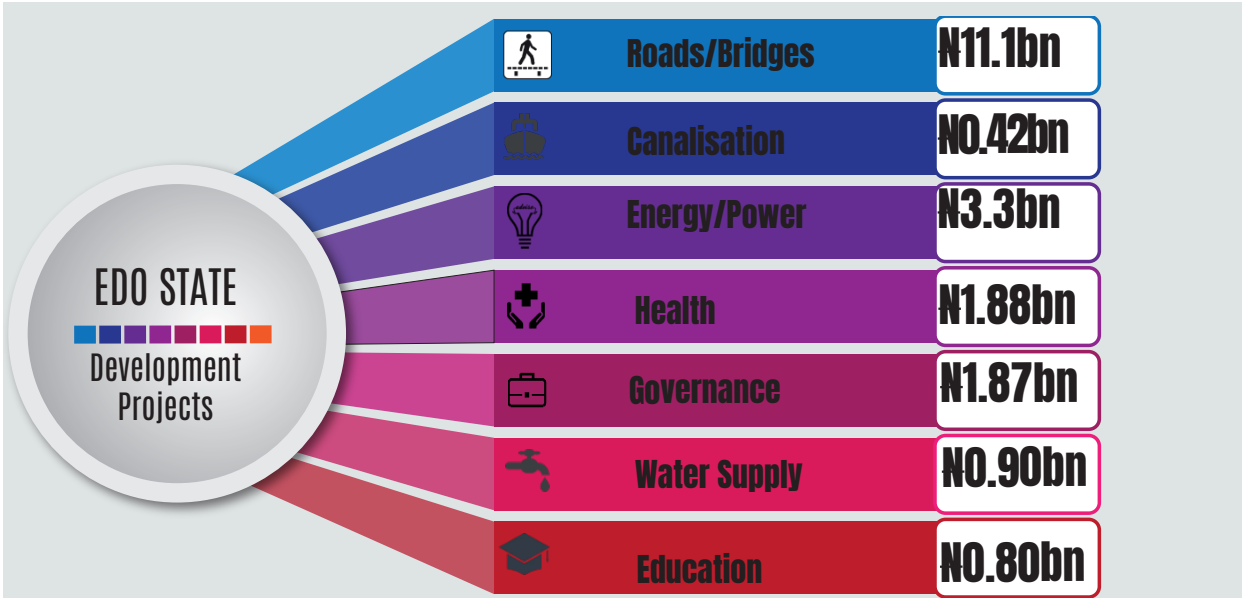

Vague and Frivolous Projects in Edo State

Reconstruction and renovation of primary and Secondary schools in Edo state Reconstruction and renovation of primary and Secondary schools in Edo state	Rehabilitation of solar street lights and feasibility study of the total capacity of installed Renewal Energy by the NDDC
N247.9m	N37.5m
Special Medical Referral	Sensitization Workshop for Traditional Birth Attendants in Edo state (Lots 1 -3)
N310.0m	N90m
Support to capacity building workshop on strengthening and retraining of rural health care givers for quality health care delivery in various communities in Edo state (Lots 1-4)	Support to Non-Governmental Bodies on Awareness and Sensitization campaign/ workshop on women related illnesses: Breast cancer, Cervical Cancer etc in Edo state (Lots 1-3)
N112.5m	N112.5m
Support to health related awareness campaign E.g Sickle cell anaemia, Chronic Leg Ulcers, Mental Health, Diabetes, Hygiene & Sanitation ethics for young girls in various communities in Edo state (Lots 1-4)	Support to Non-Governmental Bodies on Awareness and Sensitization campaign/workshop on communicable diseases: Hepatitis, Lassa Fever etc in selected communities in Edo state (Lots 1-4)
N150m	N150m
Support to celebration of World Health Days: World Health Day Celebration, World Autism Day, World Hepatitis Day in Edo state (Lots 1-4)	Awareness campaign workshop on unwanted teenage pregnancy, prostitution and baby factory business in Edo state (Lots 1-4)
N150m	N150m
Sensitization on Covid 19 Prevention and self-care for the elderly in various Communities in Edo state (Lots 1 -2)	Supply and distribution of Deworming medication to General Hospitals in various LGAs in Edo state (Lots 1-4)
N75m	N150m
Clearing of waterways in Edo state (Lots 1-20)	Contingency provision for road repairs in some selected areas
N250m	N1.81bn
Allow for payment of certified IPCand Secondary schools in Edo state	Reconstruction and renovation of primary and 1. Youth tournament (Football) and Secondary schools in Edo state 2. Provision of written materials for pupils and students in the oil producing communities
N247.9m	N7.5m
Provision of solar powered ICT training and empowerment Centre for youths and unemployed graduates including furnishing on a build and operate basisand Secondary schools in Edo state	SConstruction of Skills Acquisition Centre, Edo state
N75.5m	N75.5m Allow for payment of certified IPC
	N1.14bn


CROSS RIVERS STATE CAPITAL ALLOCATION

Cross River State had a total budget of N12.7 billion. This represents 3% of the total NDDC Development project for the year. This also represents a ...increase in the allocation in 2019. This allocation cuts across five major sub-sectors and involves some 440 projects. A breakdown shows similar trend with the other states with allocation to Road/Bridges having the highest allocation of N7.6 billion representing 60% of the total budget allocation to the state. The critical sector of Education got a paltry N428 million while the Health sector got N1.1 billion despite the negative impact of the Covid-19 pandemic.

CROSS RIVERS STATE Development Projects

S/NO	PROJECT TYPE	NUMBER OF PROJECTS	TOTAL AMOUNT
1	Education	17	428,750,000
2	Energy/Power Supply	70	1,463,746,275
3	Health	24	1,108,671,802
4	Jetty/Shore Protection	12	368,316,929
5	Road/Bridges	255	7,666,143,127
6	Governance, social security and sports	29	1,059,027,018
7	Water Supply	33	606,823,062
Grand Total		440	12,701,478,213

A further look at the allocation shows several vague/ frivolous projects amounting to N2 billion; For instance, there are vague projects with no details of location or beneficiary communities. These include *“Allow for payment of certified IPC”* with N455million allocation; *”Support to celebration of World Health days: World Health Day celebration, World Autism Day, World Hepatitis Day in cross River state”* with N112million; *“Rehabilitation of solar street lights and feasibility study of total capacity of installed renewal Energy by the NDDC”* with N37million in budgetary allocation etc.

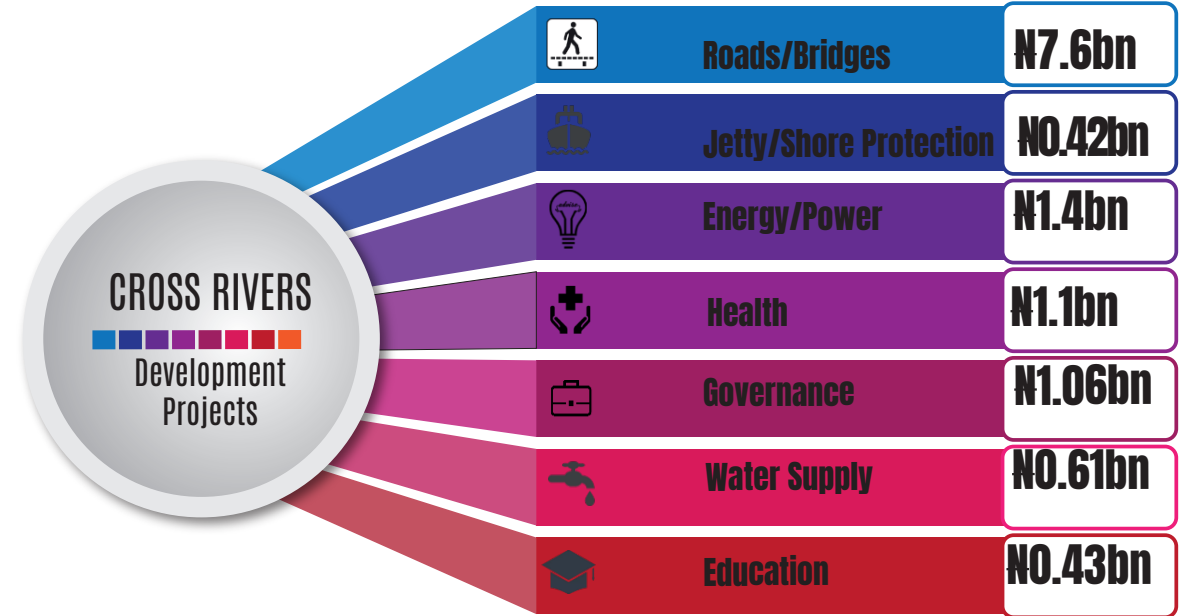

Vague and Frivolous Projects in Cross Rivers

Rehabilitation of solar street lights and feasibility study of total capacity of installed renewal Energy by the NDDC

N37.5m

Allow for payment of certified IPC

N455.6m

Construction of Solar mini grid and retrofitting of lights to energy efficient lights to power only lighting point in the House of Assembly in Cross River state

N37.5m

Provision of classroom lockers, chairs, textbooks, exercise books for primary and secondary schools in cross river central senatorial district (Lots 1-3)

N112.5m

Awareness campaign workshop on unwanted teenage pregnancy, prostitution and baby factory business in Cross River state (Lots 1-4)

N150m

Supply and distribution of deworming medication to general hospitals in various LGAs in Cross River central senatorial district, Cross River state (Lots 1-4)

N150m

Provision and Installation of solar street lights across the central senatorial district of Cross River state. (Lots 1-2)

N75m

Special Medical Referrals and check-up for the state

N30m

Construction of Mega school structure 1no. 12 classroom block, 1no. ICT block, 1no. library block, fencing and provision of 17.5 Generator and Generator house at GSS

N15m

Support to celebration of World Health days: World Health Day celebration, World Autism Day, World Hepatitis Day in cross River state (Lots 1-3)

N112.5m

Sensitization on Covid 19 prevention and self-care for the elderly in various communities in Cross River state (Lots 1-4)

N150m

Contingency provision for road repairs in some selected communities.


N180m

IMO STATE CAPITAL ALLOCATION

The Imo state 2020 NDDC Development Budget was N15.2 billion, representing about 4% of the total capital budget. The budgetary provision covered seven major subsectors with a total of 627 projects. A closer analysis shows that the subsector of Roads and Bridges with 353 projects got 57% of the total budgetary allocation. This was followed by Governance and Security with 85 projects and N2.4 billion allocation while Energy and Power with 85 projects also got N2.2 billion.

IMO STATE Development Projects

S/NO	PROJECT TYPE	NUMBER OF PROJECTS	TOTAL AMOUNT
1	Education	23	347,683,611
2	Energy/Power Supply	85	2,231,982,772
3	Canalization	10	210,514,436
4	Health	29	873,446,199
5	Road/Bridges	353	8,890,418,720
6	Governance, social security and sports	85	2,396,886,171
7	Water Supply	42	312,405,936
Grand Total		627	15,263,337,845

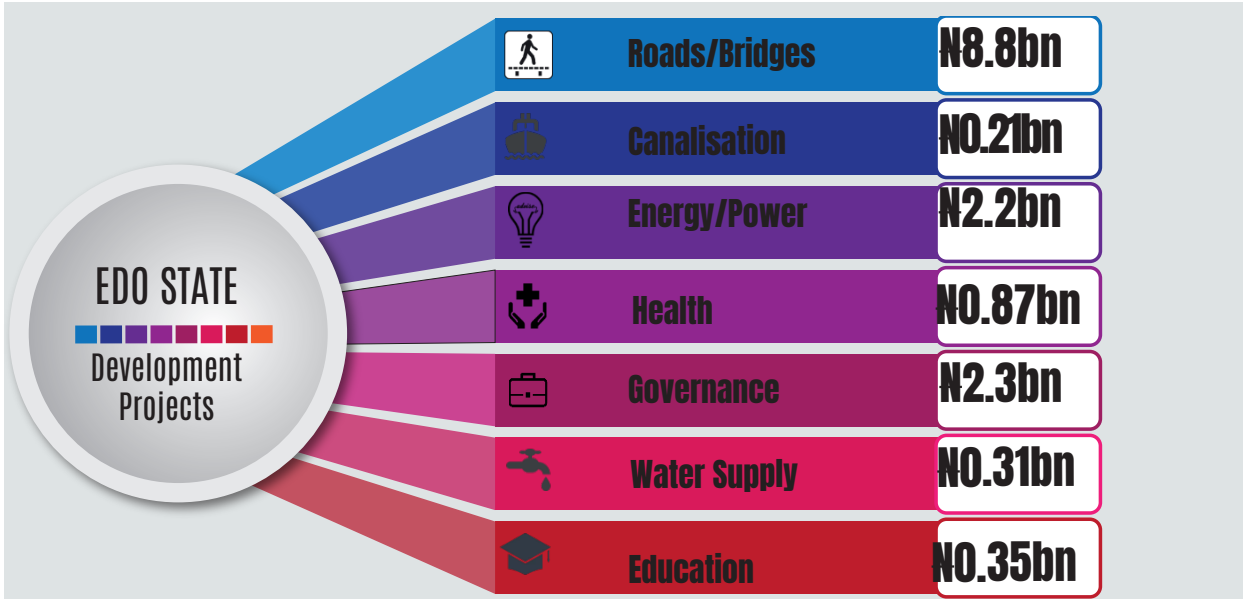

BUDGET MONITORING REPORT

Bayelsa State

Title/Location	Sector	Amount in Budget	Monitoring Report	Image Reference
Contingency Provision of clearing and desilting of blocked sessions of Azikoro 1 creek and Azikoro 2 Creek, Bayelsa State	Canalization/ Reclamation	818,946,100	Creek 1: Not properly done and uncompleted (abandoned) Creek 2: Not properly done and uncompleted (Abandoned)	Creek 1, Creak 2
Construction of one storey building Psychiatric ward at Federal Medical Centre(FMC), Yenagoa, Bayelsa state	Health Sector	37,500,000	Not Completed, building at Lintel Level	FMC1
Construction of Festus Ebi Close, off Otio road with adjoining roads (Lots 1-2)	Roads/Bridges	54,000,000	Lot 1: uncompleted, the road is tarred to the middle point. Lot 2: completed	Lot 1 , Lot 2
Construction of 1.5km concrete road of Pattos Street, opposite Saipem Yard, Elebele road, opolo	Roads/Bridges	55,125,000	Completed	Pattos 1
Construction of coconut (Okpoi) street with drains at Edepie	Roads/Bridges	45,000,000	Road poorly done and not completed (Abandoned)	Okpoi 1
Construction of 2km internal road at the Nigerian Law School	Roads/Bridges	37,500,000	Road poorly done and not completed; road constructed at the back(outside) of law school fence	Law School Road
Provision of solar street-light in AgudamaEpie, Royal FM road	Energy/Power Supply	30,240,000	Completed but report from interviewee said the lights are no longer functional, blackout at the entire street at night	Royal FM Road

Title/Location	Sector	Amount in Budget	Monitoring Report	Image Reference
Contingency provision for emergency 4KM 11KV overhead lines single circuit to evacuate power from NIPP 1X 15MVA, 33/11KV Injection substation at Opolo, reconducting and trace clearing from the Yenagoa network reconfiguration and construction of 2Nos 33KV Feeder from grain 2x 60MVA 132/33KV Transformers station to split the existing Tungbo 33KV feeder Imiringi 11/33KV feeder (Lot3)	Energy/Power Supply	149,576,205	NO ACCESS/NOT AVAILABLE	
Clearing and desilting of Korama creek, Yenagoa LGA	Canalidation/ Reclamation	91,295,385	Job not executed	Koroma Creek
Construction of 2 storey CSSD block of Federal Medical centre(FMC), Yenagoa, Bayelsa state	Health	37,500,000	NOT AVAILABLE/NOT ACCESSIBLE	
Supply of Medical equipment to federal medical centre (FMC), Yenagoa, Bayelsa State.	Health	225,000,000	NOT AVAILABLE/NOT ACCESSIBLE	
NDDC uncompleted project in Otuesega. Construction of NDDC model six classrooms block with an office, a store and VIP toilet. Bayelsa State	Education	5,883,429	Uncompleted project in Otuesega	Classrooms Block 1
Contingency provision for emergency network and reconfiguration in Yenagoa to deload Imiring 11/33kv feeder (Lot 2).	Educatio	149,700,000	Unavailable/Not executed	
Construction of perimeter fencing of NDDC staff estate phase 1	Education	72,000,000	Unavailable/Not executed	
Dredging of Atubu creek	Dredging and Construction	24,765,800	Unavailable/Not executed	

Title/Location	Sector	Amount in Budget	Monitoring Report	Image Reference
Bayelsa state school of health technology, Otuogidi	Education	10, 530,365	The building has been roofed without equipment	Otuogidi
Onuegbum town, construction of perimeter fencing of secondary school K, with an office, store and VIP toilet.	Education	42,754,630	Not executed/unavailable	
Aleibiri community in Ekeremor LGA, Shore protection project	Dredging and Construction		Not executed/unavailable	Aleibiri 1
Rehabilitation of 33kbn from Kaima to Adagbabiri 60km route length.	Roads/Bridges	24, 711,660	Not executed/unavailable	Adagbabiri 1
Construction of teachers quarter at Ebidebiri community	Education	16,500,000	Completed	Ebidebiri 1
Sand filling and land reclamation of Adagbabiri town	Canalidation/ Reclamation	150,000,000	Not executed.	Adagbabiri 2
Construction of internal road at Osekwenike community (Lot 1-2).	Road/Bridges	60,000,000	Not accessible/Not available	

Title/Location	Sector	Amount in Budget	Monitoring Report	Image Reference
Construction of Okunbor/Use secondary school road, Egor LGA	Education	200,000,000	The traditional head says he is not aware of such project being executed in his community.	Okunbor SS Road
Solar streetlight at Evbuotubu-Ogida-Ok-horo-Uwelu spare market Evbareke-Adolor college road, Use road. (Select Evbuotubu)	Education (supposed to be under Energy/Power Supply)	250,000,000	No Street lights installed	
Solar streetlight at Evbuotubu-Ogida-Ok-horo-Uwelu spare market Evbareke-Adolor college road, Use road. (Ogida)	Education (supposed to be under Energy/Power Supply)	250,000,000	No Street lights installed	
Solar streetlight at Evbuotubu-Ogida-Ok-horo-Uwelu spare market Evbareke-Adolor college road, Use road. (Select Okhoro)	Education (supposed to be under Energy/Power Supply)	250,000,000	No Street lights installed	
Solar streetlight at Evbuotubu-Ogida-Ok-horo-Uwelu spare market Evbareke-Adolor college road, Use road. (Select Uwelu spare parts market)	Education (supposed to be under Energy/Power Supply)	250,000,000	No Street lights installed	Uwelu
Solar streetlight at Evbuotubu-Ogida-Ok-horo-Uwelu spare market Evbareke-Adolor college road, Use road. (Select Evbareke)	Education (supposed to be under Energy/Power Supply)	250,000,000	No Street lights installed	Evbareke
Solar streetlight at Evbuotubu-Ogida-Ok-horo-Uwelu spare market Evbareke-Adolor college road, Use road. (Select Adolor college road)	Education (supposed to be under Energy/Power Supply)	250,000,000	No Street lights installed	Adolor 1

Title/Location	Sector	Amount in Budget	Monitoring Report	Image Reference
Solar streetlight at Evbuotubu-Ogida-Ok-horo-Uwelu spare market Evbareke-Adolor college road, Use road. (Select Use Road)	Education (supposed to be under Energy/Power Supply)	250,000,000	Completed and Functioning	College Road 1
Solar streetlight at Ugbor Amagba Village road	Energy/Power Supply	250,000,000	Completed and Functioning	Amagba 1
Construction of 600 meter perimeter fence, gatehouse, landscaping and supply of equipment and furniture to Imiegba cottage hospital.	Health	100,000,000	No perimeter fence, gatehouse, landscaping, equipment and furniture found.	Cottage Hospital1, Cottage Hospital 2
Construction of 1.2km road Airoghionba street, off Igun street, Benin Roads/Bridges	Roads/Bridges	250,000,000	Road not constructed	Igiun
Construction of Okabere road, upper Sokponba road (Phase 1)	Roads/Bridges	220,000,000	It was completed since 2018	Sokponba
Solar streetlight at Etete-Uzebu-Ihogbe-Og-be-Owina street, Erie-Oza street. (Select Etete)	Education (supposed to be under Energy/Power Supply)	250,000,000	Done	Etete
Construction of ICT centre at Benin City in Oredo LGA (relocated to Edo college, Benin city)	Education	70,461,465	The Principal says no new project construction, however, there is an uncompleted ICT centre by NDDC that was abandoned since 2011/2012. (pictures attached)	ICT
Renovation of 4 blocks at Eyaen Nogie Primary school	Education	120,000,000	Such renovation was not carried out. The only renovation noticed was done by UBEC which was more than 4 blocks.	UBEC

Title/Location	Sector	Amount in Budget	Monitoring Report	Image Reference
Rehabilitation of 2 school blocks at Trinity High School Oguta in Oguta LGA	Education	45,000,000 amount approved – 6,750,000	At the school we met the Vice Principal academics Mr. Nnan-na Edmond C. who confirmed that that was no NDDC project going on in the school. The reroofing of the school as seen in the picture is was done by the school Old Boys Association	Trinity High School
Provision of solar powered streetlight in Ndi-Ikwuegbu Oguta in Oguta LGA	Power and Energy	250,000,000; amount approved – 37,000,000	Mazi Ethelbert Asielu, who is the village chairman of Nde Ukwuegbu said there was nothing like solar energy in their community	Oguta2, Oguta3
Construction of Okonya/ Justice Asieme Road in Oguta LGA	Roads/Bridges	220,000,000; amount approved – 33,000,000	Road work was abandoned after priming state.	Oguta4
Construction of Comprehensive Health Care Centre in Otiti Omuma Oru East LGA	Health	N245,000,000; amount approved – N37,500,000	The Etiti (Otiti) has no health Care Centre before now and there was no new one in sight according to the President General of the community Mr. Tobias Nwosu.	HCC1, HCC2
Construction of Health Centre in Ubi in Oguta LGA	Power/Energy	N150,000,000; amount approved – N22,500,000	In Ubi which is a farm settlement of Oguta, the two buildings were seen; one was a health centre that was rehabilitated by Nigerian Agip oil Company and partners. The other was a building the community believed to be a health center, but had no knowledge the source of funding and there was no signpost to indicate the actual project	HCC3

Title/Location	Sector	Amount in Budget	Monitoring Report	Image Reference
Construction of Ulakwo-Umuerienwe road owerriNorth/Ngor Okala LGAs	Roads/Bridges	N400,000,000; amount approved – N60,000,000	The road construction started in 2019. Drainage started first then earth work commenced. They did the premix and since that time they have not done any other thing between 2020 and 2021 (December, 10). The community demanded that the contractors should come back to site and complete the road because they pass through untold hardship during raining season.	Okala
Construction of Okwu-Umuofor-Amaimo road in Ikeduru LGA	Roads/Bridges	N400,000,000; amount approved – N60,000,000	The primed and stone-based in 2020. After that time, no work has been done on the road till 9th December 2021, when our Team monitored the project. A community leader in Umuofor community, Mr Ugo Richard confirmed to us that due to the economic value attached to the road, some rich people in the community have volunteered themselves to work on the road but they were stopped by Abuja based politicians from the LGA.	Amaimo
Provision of solar powered light in Umuobisirke in Ahiazu Mbaise LGA	Power/Energy	N150,000,000; amount approved - N22,500,000	The lights were provided in the community.	Mbaise
Construction of Okonya/ Justice Asieme Road in Oguta LGA	Roads/Bridges	N220,000,000; amount approved – N33,000,000	Road work was abandoned after priming state	Okonya
Renovation of community primary school, Umuelem in Aboh Mbaise LGA	Education	200,000,000; amount approved – N30,000,000	The renovation of the school block just started in November, 2021 with workers sighted in the site.	Umuelem

Ondo State

Title/Location	Sector	Amount in Budget	Monitoring Report	Image Reference
Canalization of Oku-rudu/Odojomu/Odosida River in Londo, Ondo West LGA.	Canalization / reclamation	250,000,000 37,500,000	The project is yet to be completed, stopped at lafenwa street before odojomu axis.	Odosida1, Odosida
Canalization of lisaluwa River and opening up of drain gutters into Lisaluwa Rivers in Ondo City, Ondo West LGA.	Canalization / reclamation	250,000,000 Approved 37,500,000	The project is yet to be completed; the dredging stopped at Lafenwa street before Odojomu axis.	Lisaluwa 1, Lisaluwa 2
Rehabilitation and furnishing of school buildings at Ondo boys high school, Ondo City Ondo West LGA	Education	100,000,000 Approved 15,000,000	Not in existence as the old school buildings are still in dilapidated state	ONHS1, ONHS2
Installation of 132kv transmission and line 2x30mva substation at Erinje, Okitipupa	Energy/power supply	6,073,379,900 Approved 804,748,153	Project has been initiated but yet to be completed. Report gotten from the person on site revealed that the work pace slowed down as a result of lack of fund.	Transmission Line1, Transmission Line2
2x60mva,132/33kv transformer and other ancillary work at OSUTECH Okitipupa	Energy/power supply	1,000,000,000 Approved 150,000,000	The project was initiated and completed to a considerable extent and commissioned. It powered the school and its environs for just one month after the commissioning and stopped working. Some of the wirings are yet to be completed and some transformers were seen on the floor, uninstalled.	Transformer1, Transformer2
Rural electrification of Akure-Igbatoro community in Akure North LGA, Ondo State.	275,000,000 41,250,000	Energy/power Supply	The project was carried out but in a highly substandard way. 7.5kva transmission line was installed as against the initial budget for a 30kva transmission line. Some of the cable wirings are yet to be completed. It was eventually privatized and taken over by a private sector who eventually upgraded the place to its current state	The team was prohibited from taking pictures

Title/Location	Sector	Amount in Budget	Monitoring Report	Image Reference
Solar powered street lights at Ilutitun-Okitipupa, Ondo state	Energy/power supply	100,000,000 Approved 15,000,000	Project was executed and is functioning. However, it is branded with an individual's name not branded as an NDDC project.	Solar powered1, Solar powered2
Solar powered street light along Igbisin-Olo-to-Igboegunrin Road, Okitipupa Ondo State	Energy/power supply	200,000,000 30,000,000	The project was implemented and is functioning but the few functioning only last for less than four hours	Solar powered3, Solar powered4
Construction of cancer diagnostic Osutech, Okitipupa, Okitipupa LGA	Health	150,000,000 22,500,000	Not in existence	
Construction of basic health centre at Koseru, Odigbo LGA, Akure.	Health	200,000,000 30,000,000	Not completed and building is already collapsing	BHC Odigbo
Reconstruction of ikoya junction through Oloto to Igboegunrin with erosion control at Igboegunrin bridge, Igbogbirin, Okitipupa (lots 1-3)	Roads/bridges	600,000,000 90,000,000	Work just began on the 29/11/2021	Okitipupa
Solar powered borehole-Olorunduro ,Ondo East LGA, Ondo State	Water Supply	42,825,093 6,423,764	Two NDDC branded boreholes were sited. One is partially functioning as it takes a minimum of 2weeks to pump the water into the tank. The water takes time to trickle in as the underground pipes have are all rusted. This is the reason why the water doesn't serve the whole community	

NDDC TRACKED PROJECT IMAGE GALLERY

Bayelasa State Project Images



CREEK 1



CREEK 2



FMC 1



LOT 1



LOT 2



PATTOS 1



OKPOI ROAD



LAW SCHOOL ROAD



ROYAL FM ROAD



KOROMA CREEK








CLASSTOOM BLOCK 1



OTUOGIDI

Edo State Project Images

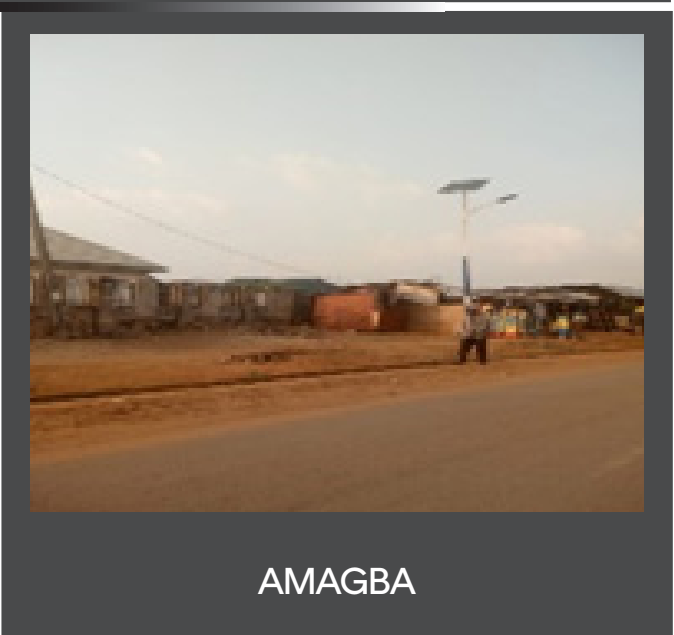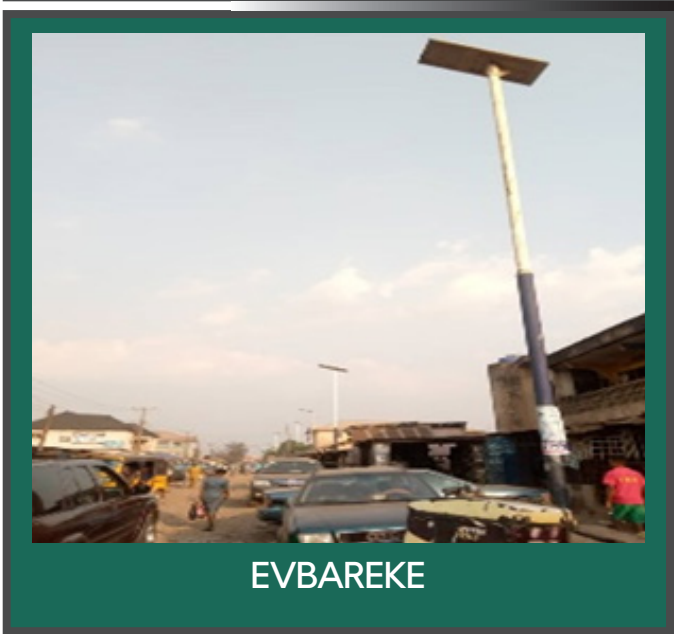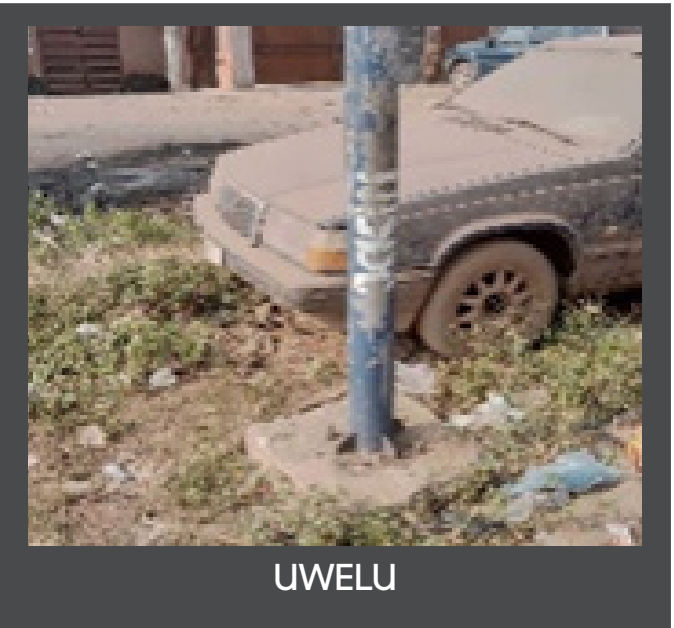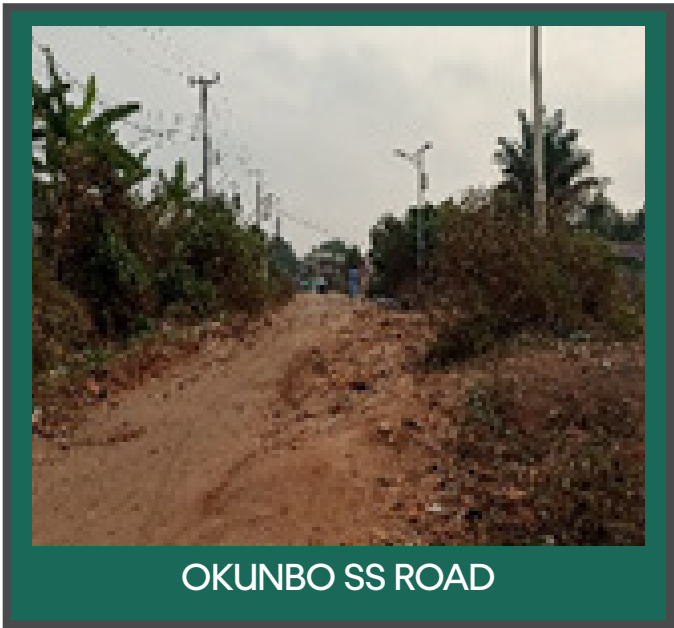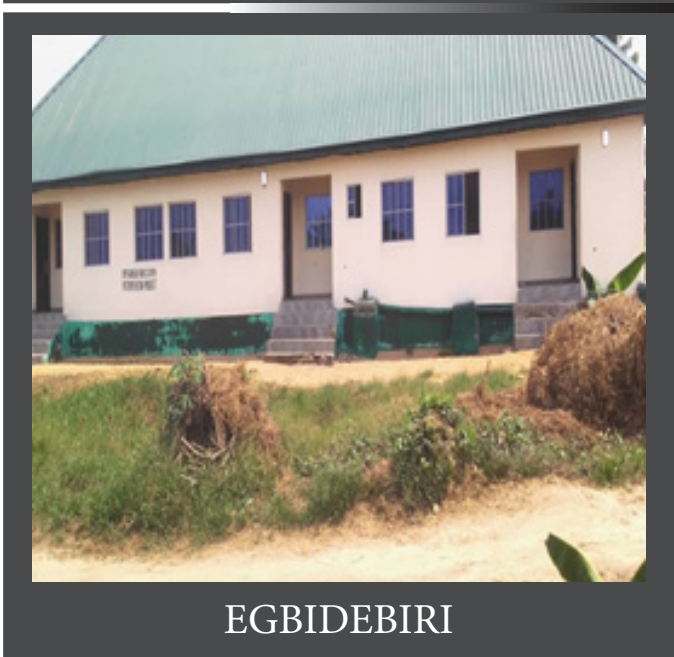



COTAGE HOSPITAL 1



CORTAGE HOSPITAL2




UBEC



IGUN



SAKPOMBA

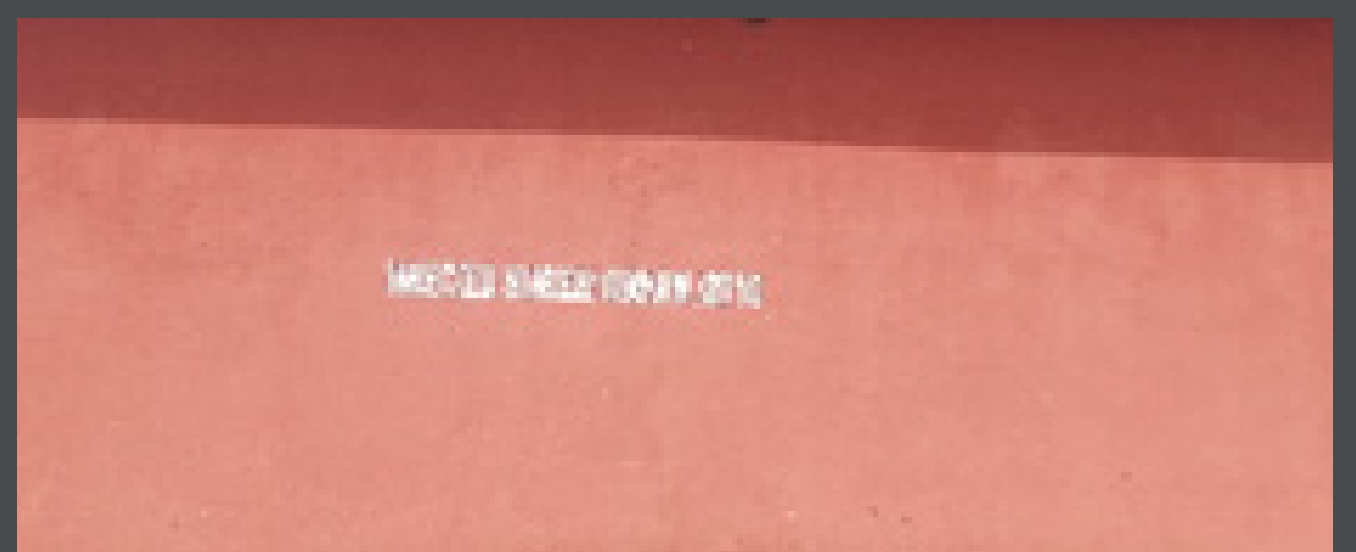

UBEC




ETETE




ICT




TRINITY HIGH SCHOOL

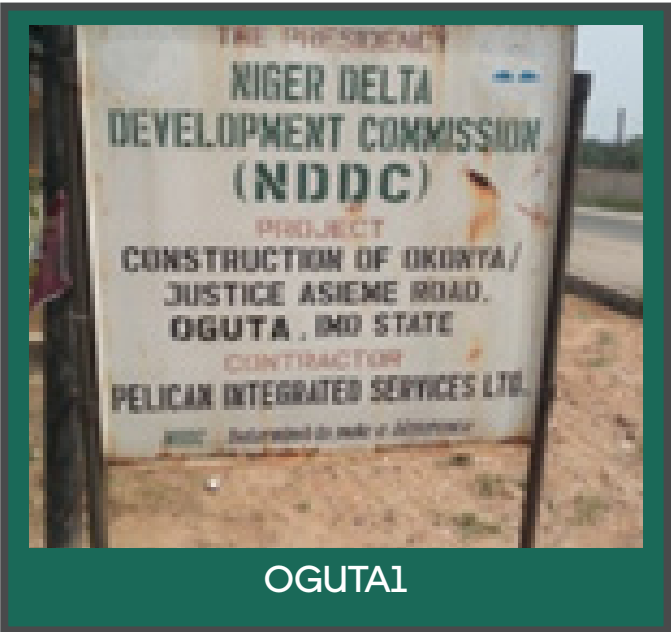


OGUTA1

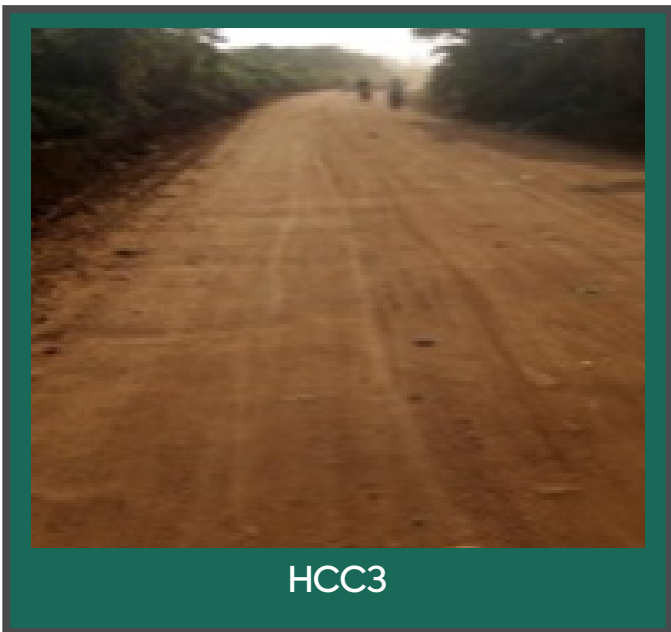


HCC3

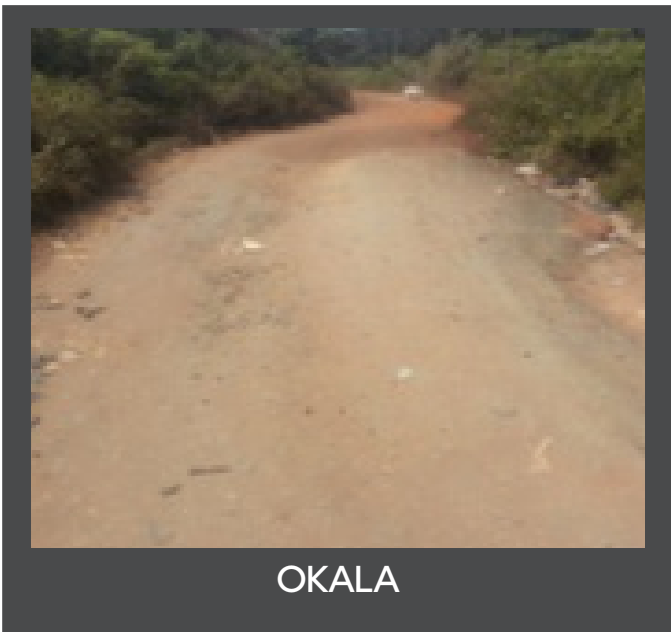

OKALA

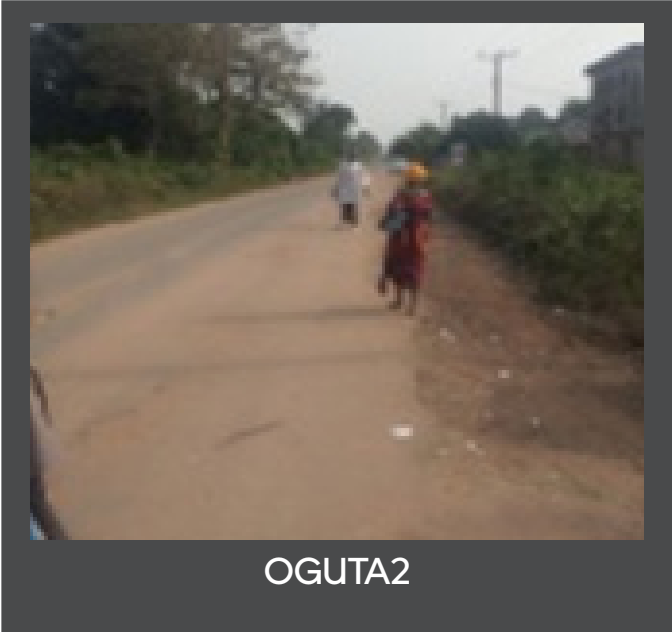

OGUTA2

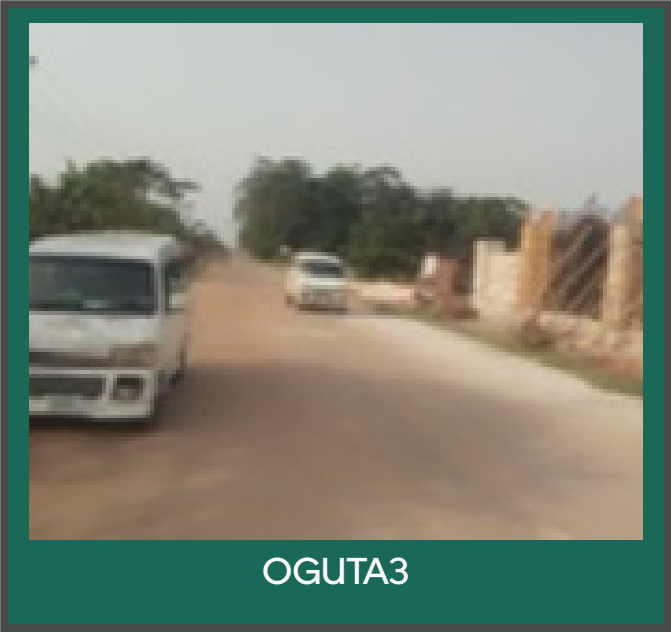

OGUTA3



AMAIMO




MBAISE




HCC1



HCC2

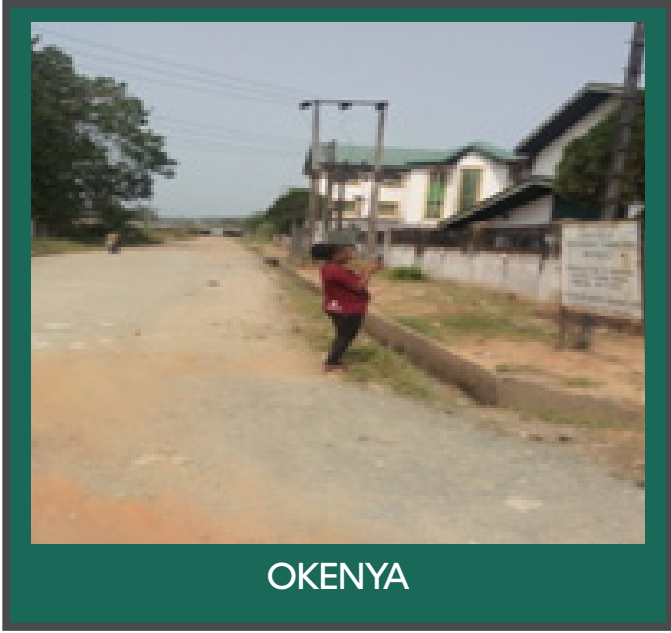

OKENYA

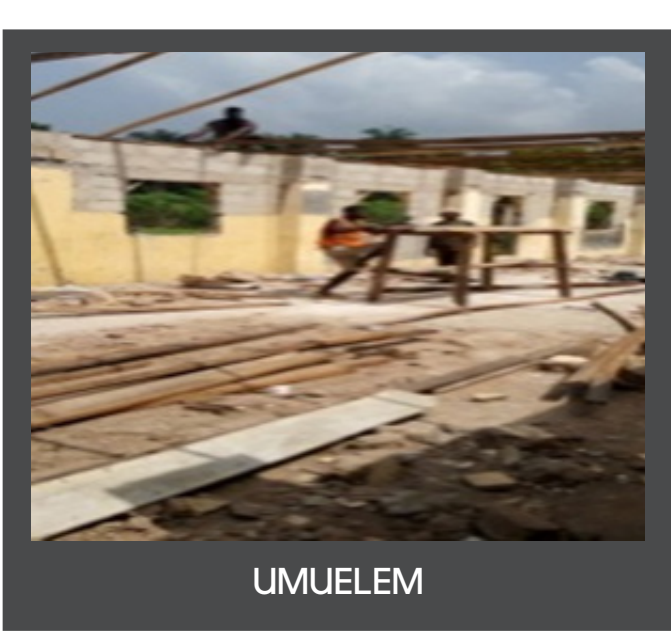

UMUELEM



ODOSIDA1



ODOSIDA1




TRANSMISSION LINE1



TRANSMISSION LINE2



LISALUWA1

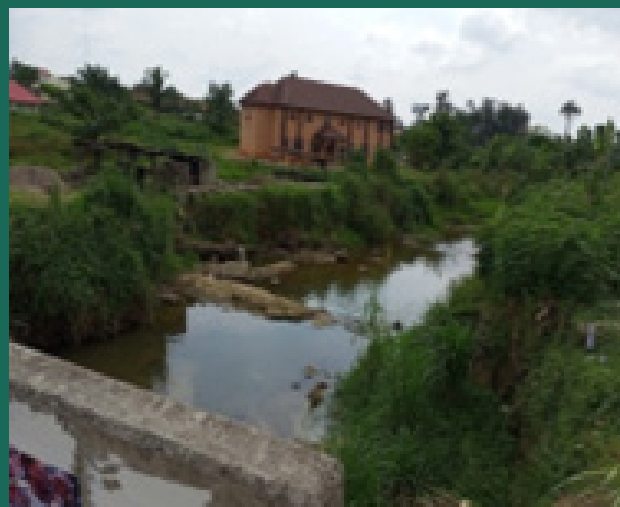

LISALUWA1



TRANSFORMA1



TRANSFORMA



OBHS1



OBHS2



SOLAR POWER1



SOLAR POWER2

Head Office

33, Oromineke Layout,
Off Emekuku Street, D-Line,
Port Harcourt, Nigeria.
Tel:+234 (0)84 360903

National Advocacy Centre
20 Yalinga Street (House1)
Wuse2, Abuja, FCT

Paralegal/Community Resource Centre Warri

No 10, Major Dan Azubuike Road,
Off Niger Cat, by Refinery Road.
Ekpan, Effurun, Warri, Delta State

Bori(Ogoniland)

6 Kaani Road (Top Flour)
Bori, Rivers State

Diobu

No 77 Urualla Street,
Mile 1 Diobu, Port Harcourt, Rivers State

Brass

JBA Villa, Twon Brass,
Bayelsa

Social Action International

310 Dupont St. Suite 200,
Toronto, ON, Canada M5R 1V9



SocialActionNigeria



SocialActionNg



Social.Action.Sdic

www.saction.org
